



Project Charter

From Waste to Worth



CSC 375 Introduction to Systems Analysis

Team 3, Learning in Progress

Table of Contents

Section 1.	Charter Introduction	2
1.1	Document Change Control	2
1.2	Executive Summary	3
1.3	Authorization.....	4
Section 2.	Project Overview	5
2.1	Project Summary	5
2.1.1	Context	5
2.1.2	Need	5
2.1.3	Project Goals, Business Outcomes and Objectives	6
2.1.4	Project Scope Definition.....	6
2.1.5	Boundaries	7
2.2	Stakeholders.....	7
2.3	Milestones	8
2.4	Deliverables.....	10
2.5	Project Cost Estimate and Source of Funding.....	12
2.5.1	Project Cost Estimate	12
2.5.2	Source of Funding	12
2.6	Dependencies.....	12
2.7	Project Risks, Assumptions, and Constraints	12
2.7.1	Risks.....	12
2.7.2	Assumptions.....	13
2.7.3	Constraints	14
Section 3.	Project Organization.....	15
3.1	Project Governance	15
3.2	Work Breakdown Structure	16
3.2.1	Project Planning	16
3.2.2	Requirements and Analysis.....	16
3.2.3	System Design.....	16
3.2.4	Project Completion.....	16
3.3	Project Team Structure	16
3.4	Roles and Responsibilities	17
Section 4.	Internal Project Documents	17
Section 5.	Glossary and Acronyms	17
Section 6.	References.....	18

Section 1. Charter Introduction

1.1 Document Change Control

Revision Number	Date of Issue	Author(s)	Brief Description of Change
1.0	01-Oct-2026	Bowen Zhang	Initial draft Drafted 1.2, 2.1, 2.4, 2.6, 2.7
1.1	02-Oct-2026	Michal Dvoracek	Drafted 2.1, 2.2, 2.3, 2.6.3, 3.1, 3.2, 3.3,
1.2	04-Oct-2026	Marissa Bumagat	Drafted review, Stakeholders
1.3	05-Oct-2026	Iris Ho	Drafted review, scope define, typeset, project progress alignment
1.4	05-Oct-2026	Bowen Zhang	Overall review and formatting

1.2 Executive Summary

The From Waste to Worth project focuses on improving food redistribution around the UVic campus. Food services may have prepared food and other edible surplus that is still suitable for consumption. However, some of this food has a short remaining usable life. The current redistribution process may rely on emails, messages, and other informal communication. This can make it difficult to coordinate donations and pickups before the food is no longer usable.

The proposed system will provide a common workflow for food redistribution. It will support surplus food recording, donation eligibility checks, recipient coordination, pickup and transportation, donation tracking, and reporting. The initial scope focuses on selected food services, the redistribution program, and a limited number of redistribution partners around the UVic campus. The project covers the analysis and design of the proposed system. Development and deployment of a production system are outside the current scope.

The project will produce a set of deliverables that define and describe the proposed system. These include the RFP, Project Charter, Requirements Document, Use Cases, Data Model, Process Model, UI Prototype, Final Report, and Project Presentation. The project is planned to progress from requirements analysis in October to the final report and presentation in November.

The main project risks include changing or incomplete requirements, limited project time, different needs between participating organizations, limited domain knowledge, and team coordination. These risks will be monitored throughout the project. No direct financial funding is required for the current project. The main resource is the time contributed by the project team members.

1.3 Authorization

This project charter formally authorizes the existence of the project, From Waste to Worth, and provides the project manager with the authority to apply organizational resources to project activities described herein. If there is a change in the project scope, the project charter will be updated and submitted for re-approval.

<u>Marissa Bumagat</u>	<u>05-Oct-2026</u>
<i>Marissa Bumagat</i>	Date
Project Manager	
<i>Client Organization</i>	

<u>Bowen Zhang</u>	<u>05-Oct-2026</u>
<i>Bowen Zhang</i>	Date
System Analyst	
<i>Client Organization</i>	

<u>Iris Ho</u>	<u>05-Oct-2026</u>
<i>Iris Ho</i>	Date
Project Manager	
<i>Vendor Organization</i>	

<u>Artan Abdolrahimzadeh</u>	<u>05-Oct-2026</u>
<i>Artan Abdolrahimzadeh</i>	Date
Data Analyst	
<i>Vendor Organization</i>	

<u>Michal Dvoracek</u>	<u>05-Oct-2026</u>
<i>Michal Dvoracek</i>	Date
System Analyst	
<i>Vendor Organization</i>	

<u>Jonathan Luelfesmann</u>	<u>05-Oct-2026</u>
<i>Jonathan Luelfesmann</i>	Date
System Developer	
<i>Vendor Organization</i>	

Section 2. Project Overview

2.1 Project Summary

Food rescue platforms already operate in Canada. The most prominent is FoodRescue.ca, run by Second Harvest, through which registered food businesses post available surplus food (type, quantity, and pickup time) and registered non-profit organizations claim and collect it. FoodRescue.ca is designed as an open, national matching service between independent donors and recipient organizations.

The From Waste to Worth project addresses a different problem: the internal coordination of surplus food within one institution. It focuses on improving the redistribution of edible surplus food around the UVic campus. Food services may generate prepared food and other edible surplus that is still suitable for consumption. However, some of this food has a short remaining usable life and must be redistributed within a reasonable pickup window.

The current process may rely on emails, messages, and other informal communication. This can make it difficult to see what food is available, whether it is eligible for donation, whether a recipient can accept it, and whether pickup can be completed in time. As a result, usable food may still be discarded.

The project proposes a common system to support the food redistribution process. The system would help participating organizations record surplus food, coordinate redistribution activities, track donations, and maintain information about completed transfers. The proposed system is therefore not intended to replace FoodRescue.ca. Platforms of this kind can remain one of the redistribution channels available to the client, and integration with them can be considered in later phases.

2.1.1 Context

UVic food services may generate prepared food and other edible surplus that is still suitable for consumption. This food may be available for redistribution to food banks and other approved recipient organizations. However, surplus food may have a short remaining usable life and must be identified, accepted, and collected within a reasonable pickup window.

Food redistribution involves several participating groups, including food service staff, redistribution program staff, recipient organizations, and pickup personnel. The process requires information about available food, donation eligibility, recipient availability, pickup arrangements, and transfer completion to be communicated between these groups.

The From Waste to Worth project is being developed within this environment. The initial project focuses on selected UVic food services and a limited number of redistribution partners around the UVic campus. It provides the organizational and operational context for defining and designing a common food redistribution system.

2.1.2 Need

The current food redistribution process may rely on emails, messages, phone calls, and other informal communication. There is no common system for participating groups to view available surplus food, confirm donation eligibility, coordinate recipient acceptance and pickup, and track whether a redistribution has been completed.

This creates limited visibility throughout the redistribution process and increases the amount of manual coordination required between participating groups. Because surplus food may have a short remaining

usable life, delays or missing information can make it more difficult to complete redistribution within the required pickup window. As a result, edible surplus food may be discarded even when redistribution may have been possible.

A common system is therefore needed to support the redistribution workflow, improve coordination between participating groups, and maintain consistent information from the identification of surplus food through completed redistribution.

2.1.3 Project Goals, Business Outcomes and Objectives

The main goal of the project is to improve the coordination and visibility of surplus food redistribution around the Uvic campus. The proposed system will provide a common workflow that connects food services, redistribution program staff, recipient organizations, and transportation personnel.

No.	Goals	Objectives	Business Outcomes
1	Improve the recording and management of surplus food.	- Allow staff to record food type, quantity, availability, pickup location, and expiry or pickup time. - Support food categorization and donation eligibility checks.	- Improve visibility of available surplus food. - Reduce avoidable disposal of edible surplus food.
2	Improve coordination between food services and recipient organizations	- Connect participating food services with approved recipient organizations. - Allow recipients to review available food and decide whether they can accept it within the required time.	- Reduce manual coordination between participating organizations. - Improve recipient access to available surplus food.
3	Improve pickup and transportation coordination.	- Provide pickup personnel with the information needed for collection and delivery. - Allow pickup personnel to confirm when food has been collected and delivered.	- Improve visibility of pickup and delivery activities. - Reduce coordination problems during time-sensitive redistribution.
4	Improve tracking and reporting of food redistribution.	- Track each donation through the redistribution process. - Maintain completed redistribution records for reporting.	- Improve visibility throughout the redistribution process. - Provide better records for food-waste and sustainability reporting.

2.1.4 Project Scope Definition

The project will define and design a food redistribution management system for participating food services and redistribution partners around the Uvic campus. The system will provide a common workflow for managing surplus food from identification to completed redistribution.

The system will support recording surplus food, including its type, quantity, availability, pickup location, and expiry or pickup time. It will support food categorization and donation eligibility checks. Approved recipient organizations will be able to review available donations and determine whether they can accept them within the required time.

The system will also support pickup and transportation coordination. Pickup personnel will be able to access pickup and delivery information and confirm collection and delivery. Each donation will be tracked through the redistribution process using its current status. Completed redistribution records will also support reporting by managers and administrators.

The initial scope will focus on selected food services, the redistribution program, and a limited number of redistribution partners around the UVic campus. The system should allow future expansion to additional locations and participating organizations.

2.1.5 Boundaries

Activities In Scope	Activities Out of Scope
1. Analyze the food redistribution process for selected UVic food services and redistribution partners.	1. Expansion to food services or redistribution partners outside the initial UVic campus environment.
2. Define requirements for surplus food recording, eligibility checks, recipient notification, pickup coordination, transfer confirmation, and reporting.	2. Implementation of food redistribution operations outside the defined project scope.
3. Develop use cases to describe interactions between the system and its intended users.	3. Direct B2P or P2P food redistribution.
4. Develop data and process models for the proposed system.	4. Development of services for community members as direct system users.
5. Develop a UI prototype for the proposed system.	5. Development and deployment of a production system.
6. Document the proposed system and present the final project results.	6. Long-term system operation, maintenance, or future expansion.

The project will focus on the analysis and design of a food redistribution system within the initial UVic campus environment. The proposed system will support selected food services, the redistribution program, and a limited number of redistribution partners. Expansion to additional campus locations and organizations within Greater Victoria may be considered in the future but is outside the current project boundary.

Community members who receive redistributed food are beneficiaries of the system, but they are not direct users within the initial scope. Direct B2P and P2P redistribution are also considered possible future expansions and are outside the current project boundary.

2.2 Stakeholders

Primary Stakeholders			
Stakeholder	Role	Influence/ Authority	How they interact with the project
Food service and kitchen staff	Documents and records food surplus information	High	Identify and record surplus food information and complete required donation and food safety information.


Primary Stakeholders			
Food service managers	Food surplus record evaluation	High	Review surplus food records, monitor donation activity, oversee staff participation, review redistribution and waste information for their location.
Redistribution program coordinators	Coordination of food redistribution and donation activities	High	Monitor incoming donations, verify donation eligibility, coordinate with donors and recipients, manage redistribution activities, oversee donations throughout the process.
Recipient organization coordinators	Receive and accept surplus food donations	High	Receive notifications of available food, review donation details, determine whether their organization can accept a donation within the pickup window.
Pickup volunteers	Transportation of surplus food	Medium	Review assigned or available pickups, access pickup and delivery information, complete required verification steps, confirm collection and delivery.
System administrators	Maintain administrative system	High	Manage participating organizations and user accounts, maintain user roles and system rules, configure operational information, oversee system records.

Secondary Stakeholders			
Stakeholder	Role	Influence	How they interact with the project
Program management	Oversee the program	High	Review aggregated data on food waste reduction, redistribution volumes, landfill diversion, and sustainability objectives.
Campus sustainability staff	Support food waste initiatives	Medium	Review redistribution activity and food waste trends across participating locations.
Finance or administrative staff	Provide financial and administrative oversight	Medium	Review overall participation, pickup performance, recipient activity, and redistribution outcomes.

2.3 Milestones

Project Milestone	Description	Expected Date
1. Request for Proposal	Problem description, objectives, and initial scope defined and submitted	Sep 27
2. Project Charter	Project charter approved, confirming goals, scope, risks, and schedule	Oct 5

Project Milestone	Description	Expected Date
3. Project Website	Project website designed and implemented	Oct 7
4. Requirements	System requirements defined and documented	Oct 11
5. Use Cases	Use cases developed describing interactions between users and the system	Oct 25
6. Data Model	Domain/data model completed	Nov 1
7. Process Model	Process model completed	Nov 8
8. UI Prototype	UI prototype developed and reviewed	Nov 15
9. Final Report	Final report completed, documenting project outcomes	Nov 22
10. Project Presentation	Final presentation delivered to stakeholders	Nov 23

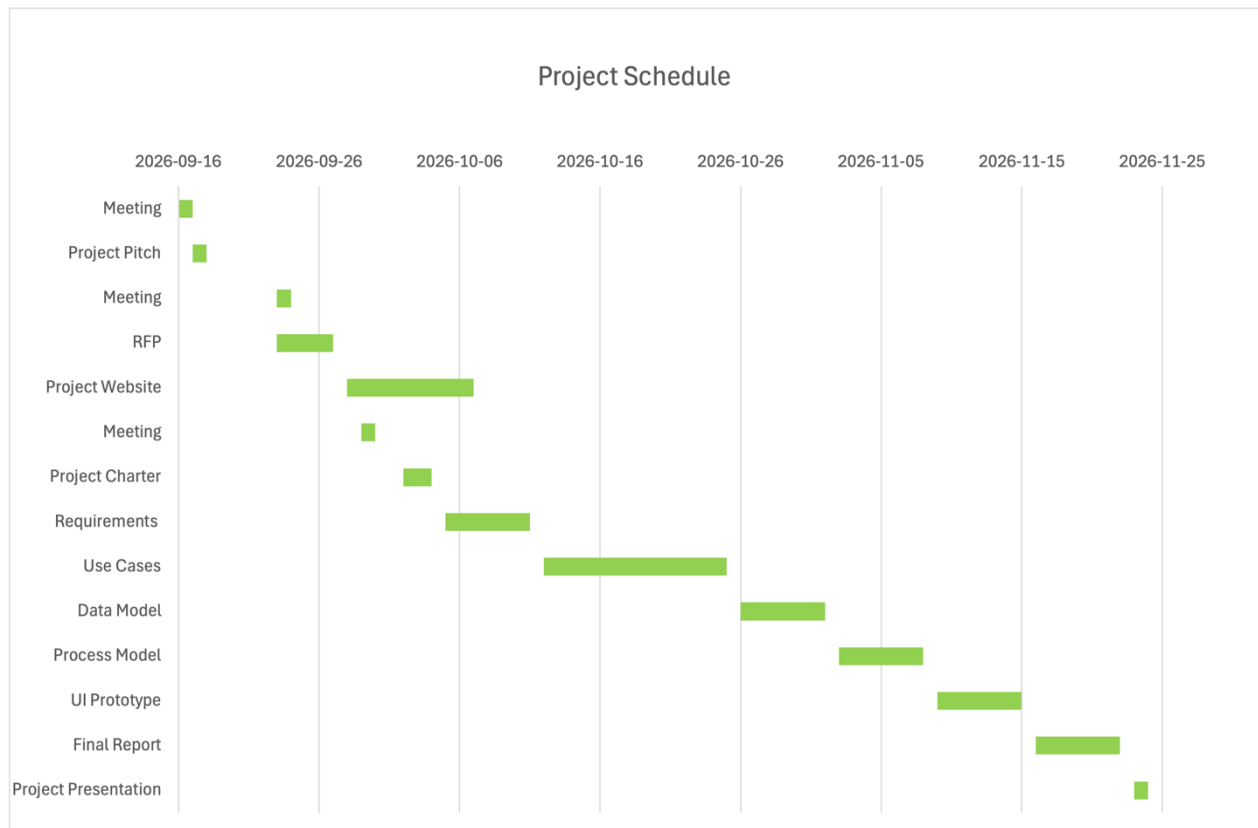

Picture 1. From Waste to Worth Project Schedule

2.4 Deliverables

Project Deliverable 1: Request for Proposal	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Defines the problem, objectives, scope, current system, intended users, and constraints of the proposed solution.
Acceptance Criteria:	RFP accepted by the client.
Due Date:	Sep 27
Project Deliverable 2: Project Charter	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Formal document authorizing the project, defining goals, scope, risks, schedule, and team organization.
Acceptance Criteria:	Charter approved by the client, confirming team roles and project boundaries.
Due Date:	Oct 05
Project Deliverable 3: Project Website	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Website introducing the project with detailed information and specifications.
Acceptance Criteria:	Website approved by both the vendor and the client teams.
Due Date:	Oct 07
Project Deliverable 4: Requirements Document	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Documents detailed functional and non-functional system requirements.
Acceptance Criteria:	Requirements accepted by the client as complete and consistent with the RFP.
Due Date:	Oct 11
Project Deliverable 5: Use Cases	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Describes interactions between intended users and the system for each major function.
Acceptance Criteria:	Use cases accepted by the client as accurately reflecting system requirements.
Due Date:	Oct 25

Project Deliverable 6: Data Model	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Defines the domain, including entities, attributes, and relationships.
Acceptance Criteria:	Data model accepted by the client as consistent with requirements and use cases.
Due Date:	Nov 01
Project Deliverable 7: Process Model	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Documents the system's process flows and workflow logic.
Acceptance Criteria:	Process model accepted by the client as accurately representing the proposed system.
Due Date:	Nov 08
Project Deliverable 8: UI Prototype	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Mock-up of the system's user interface, demonstrating usability and key functionality.
Acceptance Criteria:	Prototype accepted by the client as reflecting system requirements and use cases.
Due Date:	Nov 15
Project Deliverable 9: Final Report	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Documents the complete project outcome, consolidating all prior deliverables.
Acceptance Criteria:	Final report accepted by the client as complete and consistent with all prior deliverables.
Due Date:	Nov 22
Project Deliverable 10: Project Presentation	
Approving Stakeholder:	Marissa Bumagat (Project Manager, Client)
Description:	Presents the final project results, including the proposed system design and major project deliverables.
Acceptance Criteria:	Presentation completed and delivered to the project stakeholders.
Due Date:	Nov 23

2.5 Project Cost Estimate and Source of Funding

2.5.1 Project Cost Estimate

No monetary cost estimate applies to this project. The only resource required is team members' time, as described in Source of Funding (2.5.2).

[Phase 1/Deliverable]				
Salary	0	0	0	0
Professional Services	0	0	0	0
Capital	0	0	0	0
O&M	0	0	0	0
Ongoing cost	0	0	0	0
Other	0	0	0	0
Sub-Totals	0	0	0	0
[Phase 2/Deliverable]	0	0	0	0
Salary	0	0	0	0
Professional Services	0	0	0	0
Capital	0	0	0	0
O&M	0	0	0	0
Ongoing cost	0	0	0	0
Other	0	0	0	0
TOTAL	0			

2.5.2 Source of Funding

No direct financial funding is required for the current project. The project is completed as part of CSC 375, and the main resource is the time contributed by the project team members.

The project may use existing student resources, software, and course resources. No external funding source has been identified or committed. If the proposed system moves beyond the current analysis and design project, funding for development, deployment, operation, and maintenance would need to be determined separately.

2.6 Dependencies

Dependency Description	Critical Date	Contact
RFP acceptance is a prerequisite for Charter approval	Sep 27	Course instructor

2.7 Project Risks, Assumptions, and Constraints

2.7.1 Risks

The main project risks are related to requirements, schedule, stakeholder needs, domain knowledge, and team coordination. These risks may affect the quality, consistency, or timely completion of the project

deliverables. The project team will monitor these risks throughout the project and will take actions when needed to reduce their probability or impact.

No.	Risk Description	Probability (H/M/L)	Impact (H/M/L)	Risk Management Plan	OPI
1	Project requirements may be incomplete or change as the team develops a better understanding of the food redistribution process.	M	H	Review requirements as a team and maintain consistency between requirements, use cases, models, and the UI prototype. Control changes that affect the agreed project scope.	Project Manager / Team
2	The project may not have enough time to complete all deliverables to the expected quality.	M	H	Follow the project schedule, assign work early, monitor progress regularly, and identify delays before they affect later deliverables.	Project Manager
3	Different participating organizations may have different processes and needs, making it difficult to define one common workflow.	M	M	Keep the initial workflow simple and focus on the common activities identified in the project scope. Record organization-specific requirements separately where needed.	Business Analysts / Team
4	The team may make incorrect assumptions about food eligibility, food safety, pickup, or redistribution processes because of limited domain knowledge.	M	H	Clearly document assumptions and avoid defining unsupported operational rules. Validate important requirements with available sources or stakeholders where possible.	Business Analysts / Team
5	Team member availability or communication problems may delay dependent project tasks.	M	M	Assign responsibilities clearly, maintain regular team communication, track task progress, and redistribute work when necessary.	Project Manager / Team

2.7.2 Assumptions

The following table lists the items that cannot be proven or demonstrated when this project charter was prepared, but they are considered to stabilize the project approach or planning.

No.	Assumptions
1	Participating food services, redistribution partners, and transportation personnel are willing and able to use a common food redistribution workflow.
2	Participating users have access to suitable devices and sufficient network connectivity to use the proposed system.
3	Food-service staff can provide the required information about surplus food, including food type, quantity, availability, pickup location, and expiry or pickup time.
4	Approved recipient organizations can review available donations and respond within the required pickup window.
5	Transportation personnel are available to collect and deliver accepted donations within the required time.
6	The initial UVic campus scope is sufficient for developing and evaluating the proposed system design.

2.7.3 Constraints

The following table lists the conditional factors within which the project must operate or fit.

No.	Category	Constraints
1	Regulatory	Imposed by the regional health authority and provincial food safety requirements, with food donation guidance from the BC Centre for Disease Control (BCCDC). Eligibility checks and the information recorded for each donation (e.g., food type, preparation and storage conditions, expiry or pickup time) must follow these requirements, and donations that do not meet them must not be offered to recipients.
2	Legal	LIABILITY: The proposed system must support appropriate records for food donation and redistribution activities, including relevant donation information and eligibility checks. Applicable liability requirements and protections, including those related to the BC Food Donor Encouragement Act, will be considered during requirements analysis. The current project focuses on redistribution to approved recipient organizations and does not include the sale of donated food. PRIVACY: The proposed system should collect only the personal information needed to support food redistribution and coordination. Access to personal and operational information should be limited according to user roles. Applicable privacy requirements, including FIPPA and PIPA where relevant, will be considered during requirements analysis.
3	User Integration	The system must support users from different participating organizations. These organizations may have different procedures and technical capabilities, so the system must provide a simple and consistent workflow without requiring major changes to their existing processes.
4	Project Schedule	The project must follow the CSC 375 course schedule and complete each project deliverable by its assigned deadline.
5	Project Scope	The project is limited to system analysis and design activities defined in the charter. Development, deployment, and operation of a production system are outside the current project scope.

Section 3. Project Organization

3.1 Project Governance

The project follows a two-sided governance structure that reflects the client/vendor relationship. The Project Sponsor authorizes the project, approves this charter, and makes final decisions on changes to scope. The Client Project Manager represents the client's requirements and formally accepts each deliverable. The Vendor Project Manager manages day-to-day work, including the schedule, task assignments, and risk monitoring.

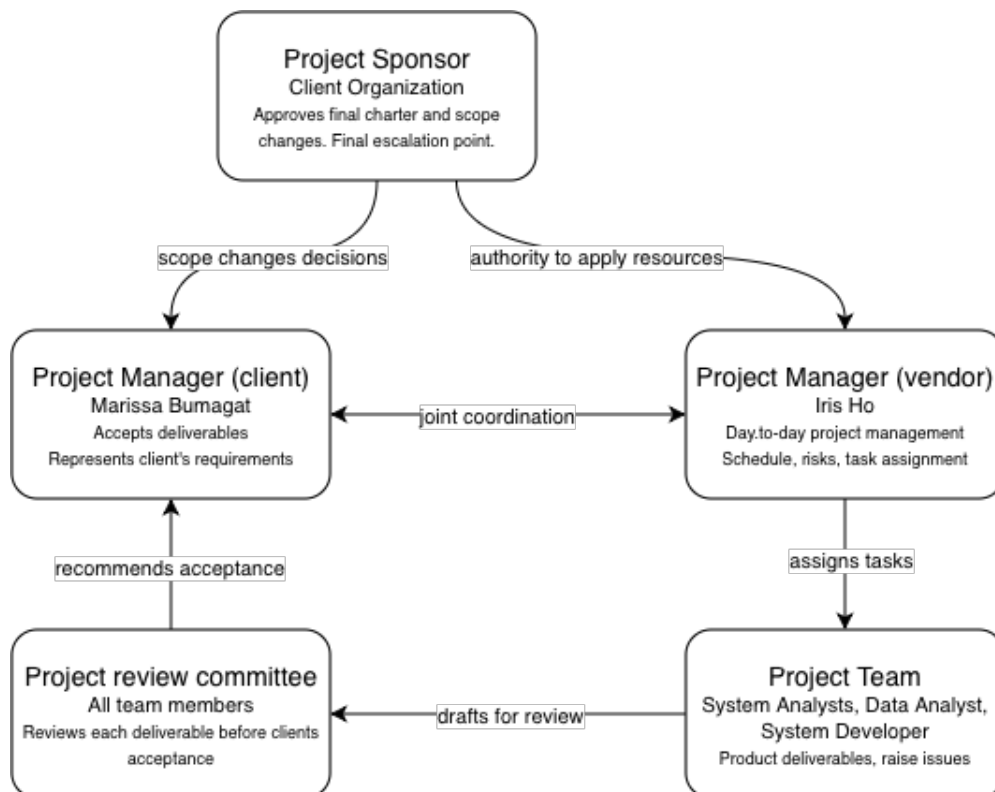


Figure 2. From Waste to Worth Project Governance Relationship

Deliverable acceptance: The project team prepares each deliverable. The Project Review Committee reviews it for completeness and consistency with previous deliverables, and the Client Project Manager accepts it.

Change approval: Proposed changes to scope or schedule are discussed by both Project Managers and approved by the Project Sponsor. Approved changes are recorded in Document Change Control, and the charter is resubmitted for re-approval.

Issue escalation: Team members raise issues with the Vendor Project Manager. Issues that can't be resolved between the two Project Managers are escalated to the Project Sponsor.

3.2 Work Breakdown Structure

3.2.1 Project Planning

- 3.2.1.1 Request for Proposal
- 3.2.1.2 Project Charter
- 3.2.1.3 Project Website Development

3.2.2 Requirements and Analysis

- 3.2.2.1 System Requirements Identification
- 3.2.2.2 Use Case Development

3.2.3 System Design

- 3.2.3.1 Data Model Development
- 3.2.3.2 Process Model Development
- 3.2.3.3 UI Prototype Development

3.2.4 Project Completion

- 3.2.4.1 Final Project Report Preparation
- 3.2.4.2 Final Project Presentation Preparation

3.3 Project Team Structure

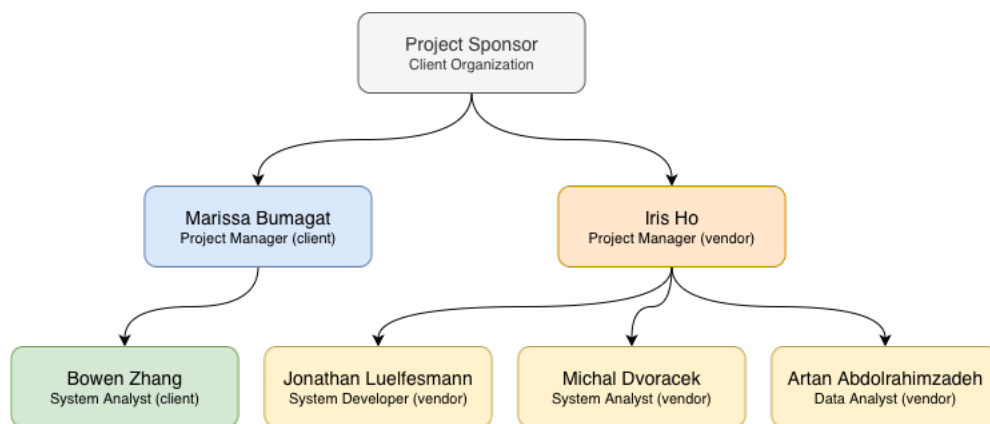


Figure 3. From Waste to Worth Project Team Structure

3.4 Roles and Responsibilities

Project Role	Responsibilities	Assigned to
Project Manager (Client)	Represents client requirements, accepts deliverables, coordinates with the Vendor Project Manager	Marissa Bumagat
Project Manager (Vendor)	Manages schedule and task assignments, monitors risks, escalates unresolved issues	Iris Ho
System Analyst (Client)	Provides client-side process knowledge, validates requirements and use cases	Bowen Zhang
System Analyst (Vendor)	Analyzes requirements, develops use cases and process models, maintains documentation	Michal Dvoracek
Data Analyst (Vendor)	Develops the data/domain model and defines data needed for reporting	Artan Abdolrahimzadeh
System Developer (Vendor)	Leads UI prototyping and reviews technical feasibility	Jonathan Luelfesmann
Project Review Committee	Reviews each deliverable for completeness and consistency before client acceptance	All team members

Section 4. Internal Project Documents

More information concerning this project can be found in the following documents:

Document Title	Version #	Date	Author and Organization	Location (link or path)
Project Charter Guide	1D	20-Mar-2008	Chief Information Officer Branch (CIOB)	See Brightspace
From Waste to Worth – Request for Proposal	1.0	27-Sept-2026	CSC 375 Team 3	See Brightspace

Section 5. Glossary and Acronyms

Term	Definition
Surplus Food	When the supply, availability, and nutritional requirements of food exceed the demand for it. It is not yet food waste and can be defined as the step before food waste.
Pickup Window	The time period during which an accepted donation is available for collection.
Food Redistribution/Redistribution Process	In the context of food, it is to store, process, then distribute surplus food while adhering to quality and regulatory frameworks.

Term	Definition
Business to Peer (B2P)	Interactions and transaction between an individual and an organization.
Peer to Peer (P2P)	Interaction and transaction between an individual and another individual.
BC Centre for Disease Control (BCCDC)	An organization in BC that monitors population health, designs and supports public health programs to prevent illness, and protects against health risks.
BC Freedom of Information and Protection of Privacy Act (FIPPA)	This act was created by BC legislation to make public bodies more accountable to the public and protect personal privacy.
BC Personal Information Protection Act (PIPA)	This act was created by BC legislation to govern the collection, use, and disclosure of personal information with regard to privacy rights of personal information.

Section 6. References

BC Centre for Disease Control. (n.d.). *What we do*.
<https://www.bccdc.ca/about/what-we-do>

Earth.Org. (2022). *What is food surplus?*
<https://earth.org/what-is-food-surplus/>

Government of British Columbia. (n.d.). *Food Donor Encouragement Act*.
https://www.bclaws.gov.bc.ca/civix/document/id/complete/statreg/00_97008_01

Government of British Columbia. (n.d.). *Freedom of Information and Protection of Privacy Act*.
https://www.bclaws.gov.bc.ca/civix/document/id/complete/statreg/96165_01#section1

Government of British Columbia. (n.d.). *Personal Information Protection Act*.
https://www.bclaws.gov.bc.ca/civix/document/id/complete/statreg/03063_01#section1

Second Harvest. (n.d.). *FoodRescue.ca*.
<https://foodrescue.secondharvest.ca>

United Nations Economic and Social Commission for Western Asia. (n.d.). *Food redistribution*.
<https://www.unescwa.org/sd-glossary/food-redistribution>
